GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE BBMP

b) Location of the Site : Byatarayanapura

c) Area of the land : Nivedithanagara 1st Main 6th Cross

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss Granite

2) Recommended Site for drilling : Ward No. 05
3) Total depth to be drilled : 1100' - 1230'
4) Approx. casing pipe required : 190' - 220'
5) No. of water bearing Zones : - 4 -
6) No. of favourable spots marked : - 10 -
7) Qty. of water expected : 2 inch
8) Method of survey carried out : Borewell
9) Remarks : 6" 12' Casing

P.T.O. : *Terms & Conditions*

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

BOREWELL SITE PLAN

Borewell site to be drilled

I, owner of the Well / (Authorised signatory) fully understand the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Manager / Proprietor

Party's Signature

Scanned by CamScanner

BOREWELL
COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

Date : _____

No. : **671**

1. Customer's Name and Address with Telephone No. : AEE BBMP Byatarayanapura Sub division

2. Well Location : Vinayakanagara I st Main 6th cross

3. Total Well Depth / Drilled in Ft. : 1211 feet

4. Casing Erected in Ft. : 194 feet

5. Water Struck at the Depth of : -

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear clear

8. At the Depth of : 1080 feet

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Thilagath

Manager / Proprietor

Party's Signature

Non Revenue cated

Scanned by CamScanner

GROUND WATER SURVEY REPORT

OPEN WELL / BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE BBMP

b) Location of the Site : Byadarayanapura SWS Level

c) Area of the land : Ashrahora layout & Maisandra

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Granite Gneiss

2) Recommended Site for drilling : Ward no. 05
3) Total depth to be drilled : 1100' - 1220'
4) Approx. casing pipe required : 180' - 210'
5) No. of water bearing Zones : - 4 -
6) No. of favourable spots marked : - 10 -
7) Qty. of water expected : 2 inch.
8) Method of survey carried out : Resistivity method.
9) Remarks : 6 1/2' DTH Drilling

HYDROGEOLOGIST
(M.G. RAJASHEKHAR. M.Sc., DEG., F.G.S.)

P.T.O. : *Terms & Conditions*

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report. I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Party's Signature

Manager / Proprietor

BOREWELL SITE PLAN

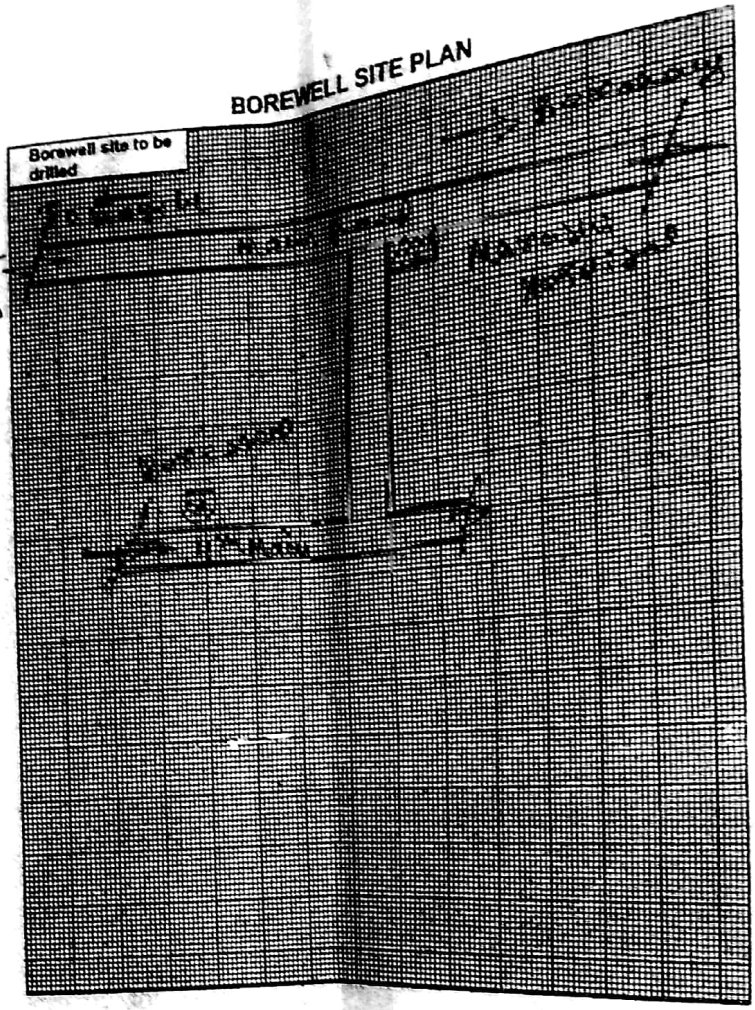

Scanned by CamScanner

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal Ring Road, Bangalore 560094

No. : 672 Date : _____

1. Customer's Name and Address : AEE BBMP
   with Telephone No. Byatarayanapura Sub division
2. Well Location : Agrahara Layout 4th main 4th cross
3. Total Well Depth / Drilled in Ft. : 1214 feet
4. Casing Erected in Ft. : 200 feet
5. Water Struck at the Depth of : —
6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)
7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear
8. At the Depth of : 1070 feet
9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Muthi

Manager / Proprietor

Party's Signature

AE ward no 5

ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

Scanned by CamScanner

BOREWELL

GROUND WATER SURVEY REPORT

OPEN WELL / BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE BBMP

b) Location of the Site : Byadarayanapa Sag

c) Area of the land : Kadrisenahalli Layout Manager

I Sr Borg.

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Granite

2) Recommended Site for drilling : Ward no. 05

3) Total depth to be drilled : 1110' - 1210'

4) Approx. casing pipe required : 180' - 200'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 10 -

7) Qty. of water expected : 200 cm

8) Method of survey carried out : Electrical method.

9) Remarks : 6/12' dia Drill up to

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : *Terms & Conditions*

BOREWELL SITE PLAN

Borewell site to be drilled

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chelapathi

Manager / ~~Proprietor~~

Party's Signature

Scanned by CamScanner

No. : 673

Date : _____

1. Customer's Name and Address with Telephone No : AEE BBMP Byatarayanapura Sub Division

2. Well Location : Kattigenahally Krishnanagara I Stage.

3. Total Well Depth / Drilled in Ft : 1207 feet.

4. Casing Erected in Ft : 190 feet.

5. Water Struck at the Depth of :

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear

8. At the Depth of : 1065 feet

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Jagathi

Manager /~~Proprietor~~

Party's Signature

Scanned by CamScanner

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AKK BBMP

b) Location of the Site : Byadarayanapura Bus Stand

c) Area of the land : Shivajinagara.

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Granite gneiss.

2) Recommended Site for drilling : Ward No. 05
3) Total depth to be drilled : 1108' - 1220'
4) Approx. casing pipe required : 185' - 206'
5) No. of water bearing Zones : - 4 -
6) No. of favourable spots marked : - 10 -
7) Qty. of water expected : 2 inch
8) Method of survey carried out : Geo physical method
9) Remarks : 6" 12' Dia Drill Bit

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O : *Terms & Conditions*

Party's Signature

I, owner of the Well / (Authorised Signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chethi

Manager / Proprietor

Party's Signature

BOREWELL SITE PLAN

Borewell site to be drilled

Scanned by CamScanner

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : **674** Date : _____

1 Customer's Name and Address with Telephone No. : AEE BBMP Byatarayanapura Sub Division

2. Well Location : Shivapura.

3. Total Well Depth / Drilled in Ft. : 1213 feet.

4. Casing Erected in Ft. : 203 feet.

5. Water Struck at the Depth of : Failure.

6. Total Yield (Measuring method "V" Norch : — / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear

8. At the Depth of : —

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chikkatti

Manager / Proprietor

Party's Signature

Scanned by CamScanner

Name of The work

ty Supply Company Limited

05/12-12-2019
·12G1Z5

Office of
Assistant Executive Engineer
C8 SAHAKARANAGARA
BESCOM
DATE: 12-12-2019

-AGE YNK

supply-NEW CONNECTION
116725113346 Dated: 10-12-2019
33548203
: regulations.
16725113346 Dated: 10-12-2019, power supply to an extent of 0 KW
nder LT basis, is hereby sanctioned, subject to the following:

	0

ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned by CamScanner

2	No. of Floors Added or New	0
3	Existing Plinth Area in sq m	0
4	Added or New Plinth Area in sq m	0
5	**Total Plinth Area in sq.m.**	0

b Total height of the building above ground level in m 0

2. The **PROPOSED** Sanctioned Load of your building is **11.19 KW**

Existing Load Details of your premises

1	Existing Sanctioned Load	0
2	New/ Additional Load Required	**0 KW and 15 HP**
3	Total Load	**11.19 KW**

You are requested to pay the following charges by Cash/ DD (above ₹10000/- only DD will be accepted) in favour of **The Assistant Executive Engineer (El) C8 SAHAKARANAGARA, BESCOM** within 30 days from the date of this letter

Sl. No	Particulars	Amount
1.	2 MMD to be for 1 Nos (of **0 KW** and **15 HP**) installation	₹13710.00
2.	MSD Amount	2020 ~~₹0.00~~
3.	Infrastructure Charges	₹0.00
4.	Service Line Cost(Development Charge)	₹0.00
5.	Additional Development /Service Line Charges	₹0.00
6.	CGST Amount	152. ~~₹0.00~~
7.	SGST Amount	152. ~~₹0.00~~
	Total	+ ₹13710.00

Note :2 MMD/MSD shall be paid separately for individual installations (separate Payment Receipts to be drawn)

3. The power supply will be arranged at 400V

4. The Power Tariff applicable to your proposed installation will be **Monthly LT6A tariff schedule for metered customers(BESCOM)** Tariff, or as in force from time to time

5. You have to confirm to purchase High precision/Electrostatic meters/ETV meters of the following capacity

Single Phase Meters _____Nos

Three Phase Meters _____Nos

548203

AEE BBMP

c) ETV Meters _____Nos

d) TP box with _____CTR _____Nos

6. After the payments the following requirements may please be fulfilled

a) Execute agreement of power supply on ₹200/- Stamp Paper in duplicable, for individual installations in the prescribed format

b) Produce necessary License/Permit/No Objection Certificate etc issued by the Competent Authority, as required under the statute

7(a) The Power supply will be arranged by **BESCOM** as below

a) From the existing _KVA Transformer

b) After enhancement of TC capacity from KVA to 0 KVA of the TC located at

c) After erecting new 0 KVA transformer under service connection

7(b) If you intend to install distribution transformer inside your premises, and execute the work under self-execution, following above power supply, the following shall be complied

i. An electrical room with RCC roof having clear floor area of 5 metres X 4 metres, with a vertical clearance of 2.75 meters with locking facility, exhaust fans and adequate size of cable duct, shall be provided at the ground floor, within the Applicant's premises nearer to the main entrance, for installing floor mounted distribution transformer and associated switchgear, or

ii. A clear space of 3 metres X 5 metres open to the sky shall be provided, within the Applicant's premises, preferably at the main entrance, for installing structure mounted distribution transformer and switchgear

8. **BESCOM** approved suitable capacity circuit breaker, ELCB & switchgears shall be used, and all the provisions under KERC Regulations 4.03 and 4.04 shall be complied

9. **BESCOM** reserves the right to cancel power supply and forfeiting of the Deposits paid by you, if the documents submitted by you are found to be fake

10 As per the Govt Order, solar water heaters of suitable capacity shall be provided

11 Five nos of Compact Fluorescent Lamps shall be used for each installation

12. The metering equipment to be installed should be conspicuously visible and at the main entrance to the premises, preferably with an independent entrance

You are requested to contact the undersigned in case of any other information that may be required by you

We remain at your services

Yours faithfully

Assistant Executive Engi

C8 SAHAKARANAGA

BESCOM

Account ID 9933548203

Consumer Name AEE BBMP

Scanned by CamScanner

--- THANK YOU ---

C7 YALAHANKA

Receipt Number	6459251029430
Receipt Date	04-12-2019 15:20:56
Cash Counter	BESCOM - C7 Yelahanka new town
Payer Account ID	6459251932
Person Name	AEE BBMP
PE Number	
Total Payment	Rs.2,211.00
Mode of pay	Draft
Cheque/DD No	622828
Bank Name	VB
Purpose	Deposits
Non Revenue category	MSD-EEE

Two Thousand Two Hundred and Eleven Rupees Only

Supply Company Limited

03-12-2019

G1Z5

--- THANK YOU ---

C7 YALAHANKA

Receipt Number	6459251195558
Receipt Date	04-12-2019 15:20:56
Cash Counter	BESCOM - C7 Yelahanka new town
Payer Account ID	6459251932
Person Name	AEE BBMP
PE Number	
Total Payment	Rs.13,710.00
Mode of pay	Draft
Cheque/DD No	622828
Bank Name	VB
Purpose	Deposits
Non Revenue category	2MMD-EEE

Thirteen Thousand Seven Hundred Ten Rupees Only

Office of
Assistant Executive Engineer
C7 YALAHANKA
BESCOM
DATE: 03-12-2019

NAGARA,

560ಆಡಳಿತಾಧಿಕಾರಿಯವರು ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Sir/Madam,

Sub: Arranging LT power supply-NEW CONNECTION

Ref: **1) Application No:208068896127 Dated: 21-11-2019**
2) Account ID : 6459251932
3) Prevailing KERC regulations.

With reference to your Application No. **208068896127 Dated: 21-11-2019**, power supply to an extent of **0 KW** and **15 HP** on Account ID **6459251932** under LT basis, is hereby sanctioned, subject to the following:

1. Details of your building/premises:

a. Plinth area:

1	No. of Floors Existing	0

Account ID : 6459251932
Consumer Name : AEE BBMP

ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned by CamScanner

2	No. of Floors Added or New	0
3	Existing Plinth Area in sq.m.	0
4	Added or New Plinth Area in sq.m.	0
5	**Total Plinth Area in sq.m.**	0

b. Total height of the building above ground level in m: **0**

2. The **PROPOSED** Sanctioned Load of your building is **11.19 KW**

Existing Load Details of your premises:

1	Existing Sanctioned Load	**0**
2	New/ Additional Load Required	**0 KW and 15 HP**
3	Total Load	**11.19 KW**

You are requested to pay the following charges by Cash/ DD (above ₹10000/-, only DD will be accepted) in favour of **The Assistant Executive Engineer (EI) C7 YALAHANKA, BESCOM** within 30 days from the date of this letter:

Sl. No.	Particulars	Amount
1.	2 MMD to be for 1 Nos (of **0 KW** and **15 HP**) installation	₹13710.00
2.	MSD Amount	~~₹0.00~~ 2211/-
3.	Infrastructure Charges	₹0.00
4.	Service Line Cost(Development Charge)	₹0.00
5.	Additional Development /Service Line Charges	₹0.00
6.	CGST Amount	₹0.00
7.	SGST Amount	₹0.00
	Total	~~₹13710.00~~ 15921/-

Note: 2 MMD/MSD shall be paid separately for individual installations (separate Payment Receipts to be drawn).

3. The power supply will be arranged at 400V

4. The Power Tariff applicable to your proposed installation will be **Monthly LT6A tariff schedule for metered customers(BESCOM)** Tariff, or as in force from time to time

5. You have to confirm to purchase High precision/Electrostatic meters/ETV meters of the following capacity:

   a) Single Phase Meters _____Nos.

   b) Three Phase Meters _____Nos.

Account ID : 6459251932

Consumer Name : AEE BBMP

Scanned by CamScanner

THANK YOU

C7 YALAHANKA

Receipt Number	9012862261[illegible]
Receipt Date	04-12-2019 15:20:56
Cash Counter	BESCOM [illegible] C7 yelahanka new town
Payer Account ID	9012862528
Person Name	AEE BBMP
RR Number	
Total Payment	Rs2,211.00
Mode of pay	Draft
Cheque DD No	622828
Bank Name	VB
Purpose	Deposits
Non Revenue category	MSD-EFF

Two Thousand Two Hundred and Eleven Rupees Only

ly Company Limited

:019

THANK YOU

C7 YALAHANKA

Receipt Number	9012862[illegible]11
Receipt Date	04-12-2019 15:20:56
Cash Counter	BESCOM [illegible] C7 yelahanka new town
Payer Account ID	9012862528
Person Name	AEE BBMP
RR Number	
Total Payment	Rs13,710.00
Mode of pay	Draft
Cheque DD No	622828
Bank Name	VB
Purpose	Deposits
Non Revenue category	MSD-EFF

Thirteen Thousand Seven Hundred Ten Rupees Only

THANK YOU

Office of
Assistant Executive Engineer
C7 YALAHANKA
BESCOM
DATE: 03-12-2019

NAHALLI(V),

YELAHANKA,
BANGALORE KARNATAKA
560064

Sir/Madam,

Sub: Arranging LT power supply-NEW CONNECTION

Ref: 1) Application No:544597056895 Dated: 21-11-2019
2) Account ID : 9012862528
3) Prevailing KERC regulations.

With reference to your Application No. **544597056895 Dated: 21-11-2019**, power supply to an extent of **0 KW** and **15 HP** on Account ID **9012862528** under LT basis, is hereby sanctioned, subject to the following:

1. Details of your building/premises:

a. Plinth area:

1	No. of Floors Existing	0

Account ID : 9012862528
Consumer Name : AEE BBMP

[illegible]

Scanned by CamScanner

2	No. of Floors Added or New	0
3	Existing Plinth Area in sq.m.	0
4	Added or New Plinth Area in sq.m.	0
5	**Total Plinth Area in sq.m.**	0

b. Total height of the building above ground level in m: **0**

2. The **PROPOSED** Sanctioned Load of your building is **11.19 KW**

Existing Load Details of your premises:

1	Existing Sanctioned Load	**0**
2	New/ Additional Load Required	**0 KW and 15 HP**
3	Total Load	**11.19 KW**

You are requested to pay the following charges by Cash/ DD (above ₹10000/-, only DD will be accepted) in favour of **The Assistant Executive Engineer (EI) C7 YALAHANKA, BESCOM** within 30 days from the date of this letter:

Sl. No.	Particulars	Amount
1.	2 MMD to be for 1 Nos (of **0 KW** and **15 HP**) installation	**₹13710.00**
2.	MSD Amount	2211/- ~~**₹0.00**~~
3.	Infrastructure Charges	**₹0.00**
4.	Service Line Cost(Development Charge)	**₹0.00**
5.	Additional Development /Service Line Charges	**₹0.00**
6.	CGST Amount	**₹0.00**
7.	SGST Amount	**₹0.00**
	Total	15921/- ~~**₹13710.00**~~

Note: 2 MMD/MSD shall be paid separately for individual installations (separate Payment Receipts to be drawn).

3. The power supply will be arranged at 400V

4. The Power Tariff applicable to your proposed installation will be **Monthly LT6A tariff schedule for metered customers(BESCOM)** Tariff, or as in force from time to time

5. You have to confirm to purchase High precision/Electrostatic meters/ETV meters of the following capacity:

   a) Single Phase Meters _____Nos.

   b) Three Phase Meters _____Nos.

c) ETV Meters _____ Nos

d) TP box with _____ CTR

6. After the payments, the follow

Account ID : 9012862528

Consumer Name : AEE BBMP

Scanned by CamScanner
